LAB 2 - AGILE PROJECT MANAGEMENT

Airport Lost Luggage Claim & Tracking Portal

Student Registration Number	PES1UG24CS579
Problem Statement	30
Primary Domain	Smart Cities, Transport & Logistics
Target Actors	Passenger; Baggage Service Agent
Jira Space	Airport Lost Luggage Portal (SCRUM)

1. Objective and Scope

The Jira workspace models a traceable airport lost-luggage recovery lifecycle. The implementation is intentionally constrained to one epic and one completed sprint, as specified for this submission.

2. Epic and Product Backlog

Epic: SCRUM-5 - Airport Lost Luggage Recovery Lifecycle

Epic intent: Enable passengers and baggage service agents to report, track, investigate, recover, return, and compensate lost-luggage claims through one auditable workflow.

Key	User Story	Priority	Points	Final Status
SCRUM-1	Submit Lost Luggage Claim	High	3	Done
SCRUM-2	Match Claim with Baggage Scan Logs	High	5	Done
SCRUM-3	Track Claim and Bag Timeline	High	5	Done
SCRUM-4	Investigate Claim and Arrange Return	High	5	Done
SCRUM-6	Process Eligible Compensation	Medium	8	Done

Total commitment: 5 user stories, 26 story points.

3. Epic and Estimation Evidence

The epic contains the five implementation stories. All stories are linked to SCRUM-5 and show their final completion state in Jira.

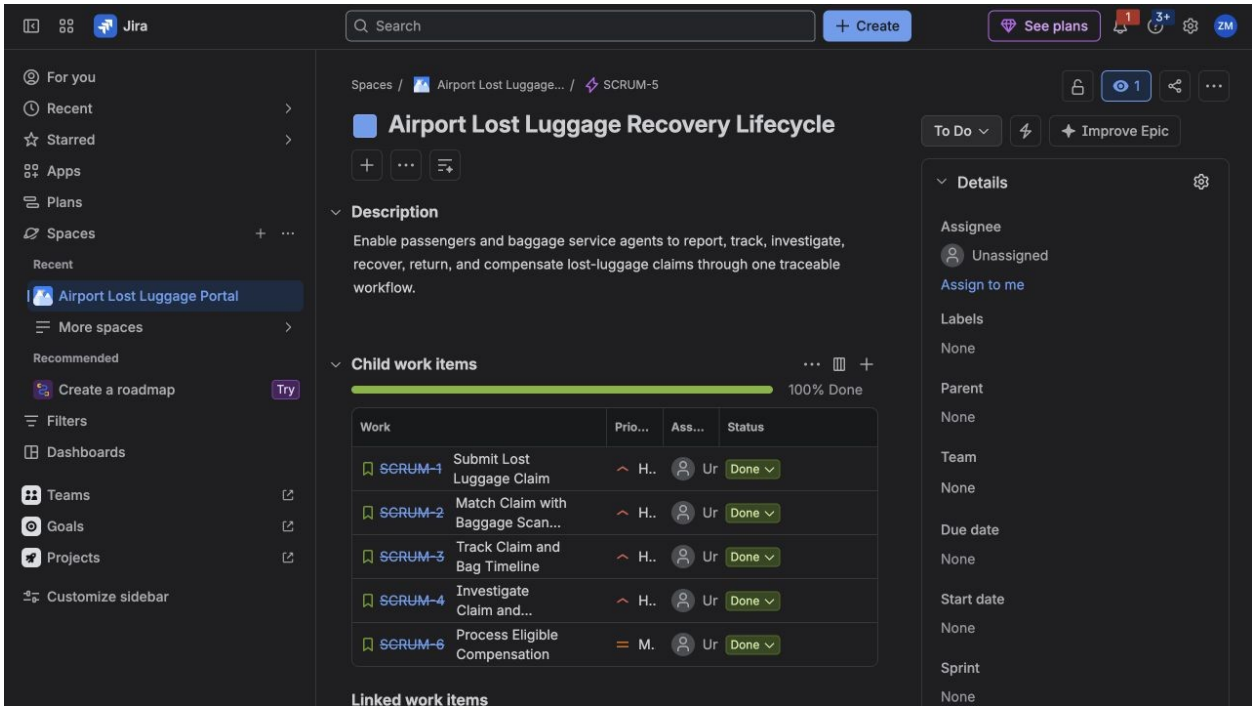


Figure 1. Jira epic and linked user stories.

3.1 Story Point Assignments

The completed-sprint report confirms the individual estimates of 3, 5, 5, 5, and 8 story points, for a total commitment of 26 points.

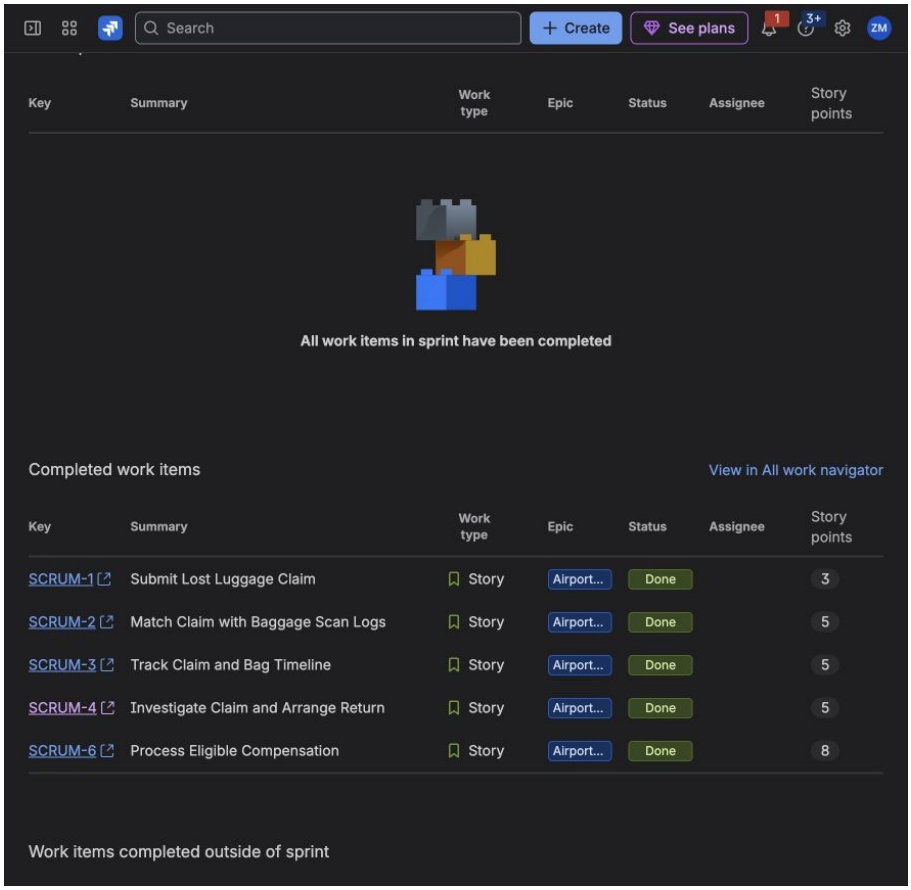


Figure 2. Jira story-point assignments for all five stories.

4. Sprint Execution

Sprint Attribute	Configured Value
Sprint	SCRUM Sprint 1
Duration	One week: 2 September 2026 to 9 September 2026
Commitment	26 story points
Workflow simulation	To Do -> In Progress -> Done
Completion	5 of 5 stories completed; 26 of 26 points delivered

The active-board evidence records the sprint in progress, with committed stories distributed across To Do, In Progress, and Done. All five stories were subsequently completed before the sprint was closed.

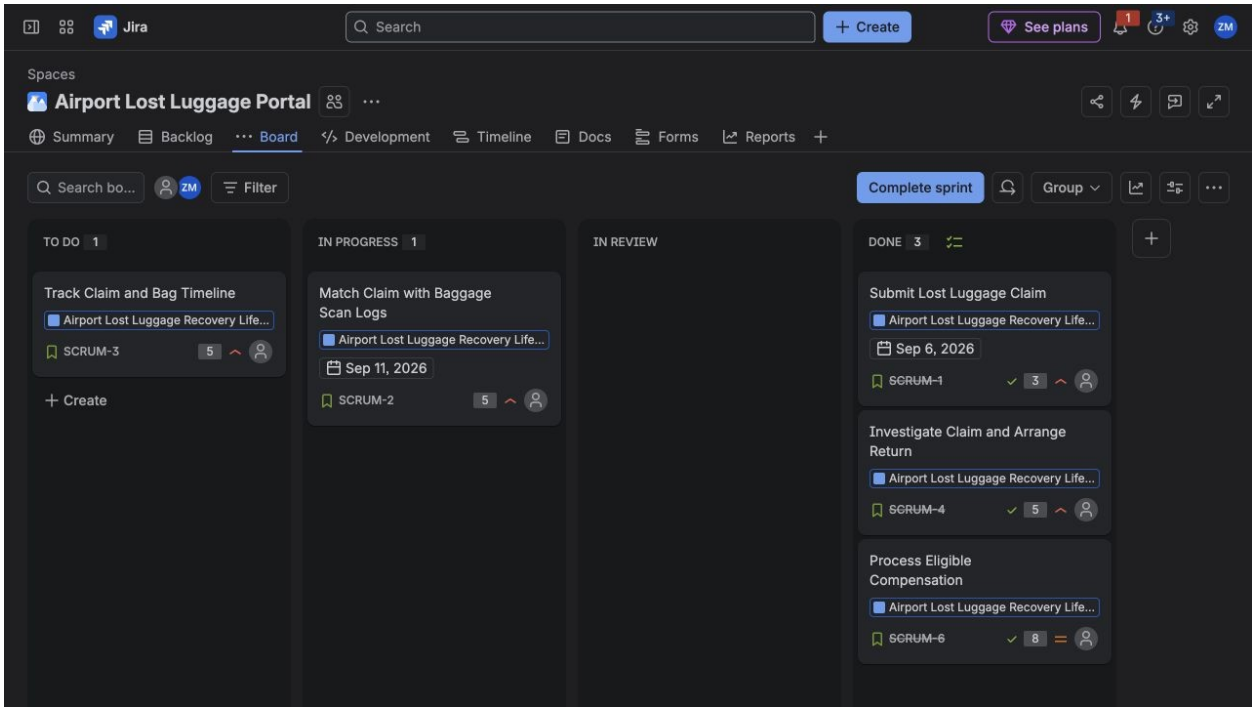


Figure 3. Jira active sprint board with work distributed across workflow states.

5. Burndown Evidence

The Jira burndown report is configured for SCRUM Sprint 1 and story-point estimation. The initial work was completed rapidly; two stories totaling 10 points were then retained in the staged workflow until the next day and completed. This produces Jira's genuine short 10-point plateau before the remaining work returns to zero.

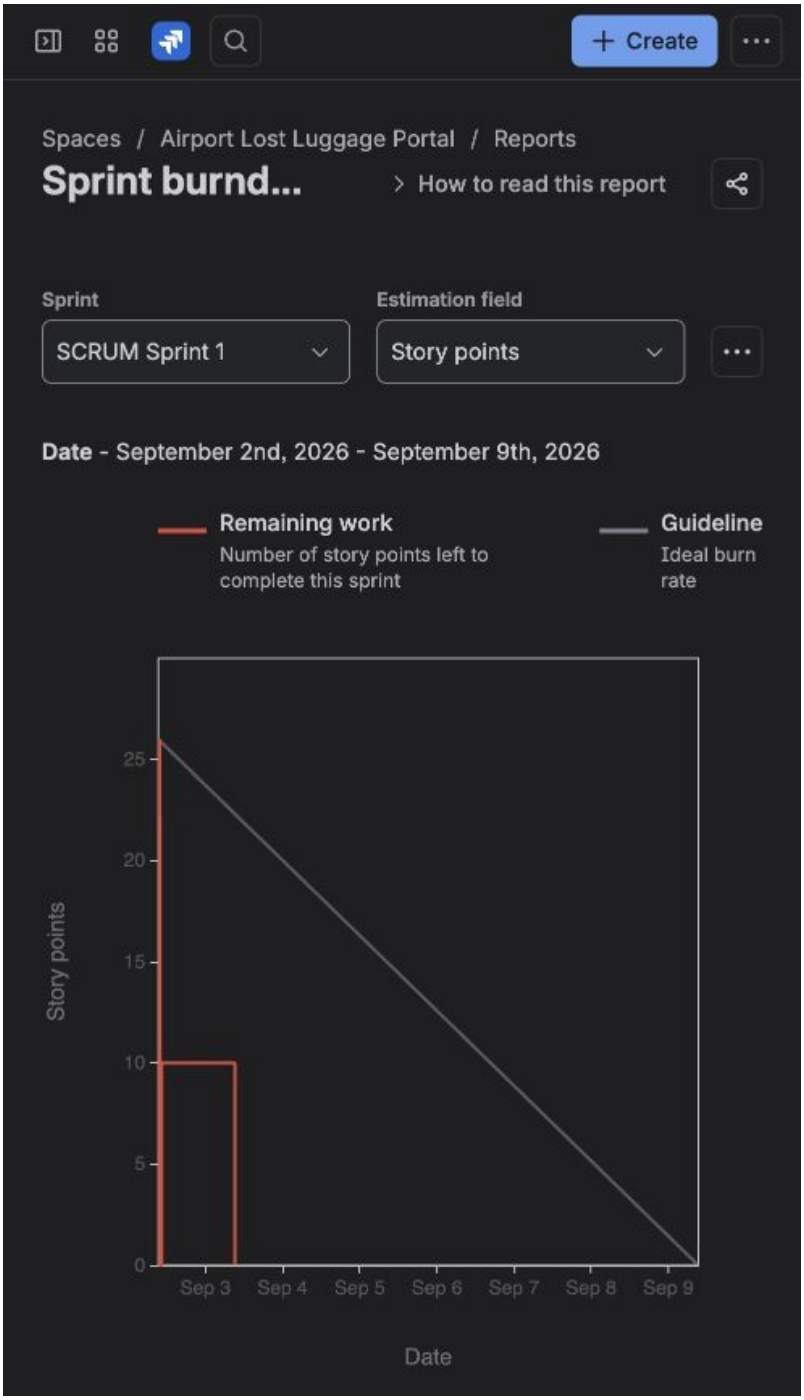


Figure 4. Jira burndown report for the completed sprint.

6. Reflection

1. Did the estimations reflect the actual effort?

Yes. The 3-point claim-submission story was the smallest bounded workflow, while scan matching, timeline tracking, and recovery coordination required more integration and validation. Compensation received the highest estimate because it combines eligibility rules, evidence checks, decision output, and payment-state handling.

2. Was the backlog well-prioritized?

Yes. High-priority work established the operational recovery path first: claim creation, scan matching, tracking, and agent-led return. Compensation followed at Medium priority because it depends on a mature, unresolved claim.

3. How did the simulated sprint align with expectations?

The sprint progressed logically from intake and scan matching to passenger visibility, agent recovery, and final compensation handling. The staged status changes made work-in-progress visible and preserved traceability before all five stories were completed.

4. What insights did the burndown provide?

The chart shows an early concentrated completion followed by a short 10-point plateau and final reduction to zero. In a real sprint, stories should be completed continuously across the timebox to provide steadier feedback and expose delivery risk earlier.
