LAB 2 - AGILE PROJECT MANAGEMENT

Airport Lost Luggage Claim & Tracking Portal

Student Registration Number	PES1UG24CS579
Problem Statement	30
Primary Domain	Smart Cities, Transport & Logistics
Target Actors	Passenger; Baggage Service Agent
Jira Space	Airport Lost Luggage Portal (SCRUM)

1. Objective and Scope

The Jira workspace models a traceable airport lost-luggage recovery lifecycle. The implementation is intentionally constrained to one epic and one completed sprint, as specified for this submission.

2. Epic and Product Backlog

Epic: SCRUM-5 - Airport Lost Luggage Recovery Lifecycle

Epic intent: Enable passengers and baggage service agents to report, track, investigate, recover, return, and compensate lost-luggage claims through one auditable workflow.

Key	User Story	Priority	Points	Final Status
SCRUM-1	Submit Lost Luggage Claim	High	3	Done
SCRUM-2	Match Claim with Baggage Scan Logs	High	5	Done
SCRUM-3	Track Claim and Bag Timeline	High	5	Done
SCRUM-4	Investigate Claim and Arrange Return	High	5	Done
SCRUM-6	Process Eligible Compensation	Medium	8	Done

Total commitment: 5 user stories, 26 story points.

3. Epic Evidence

The epic contains the five implementation stories. All stories are linked to SCRUM-5 and show their final completion state in Jira.

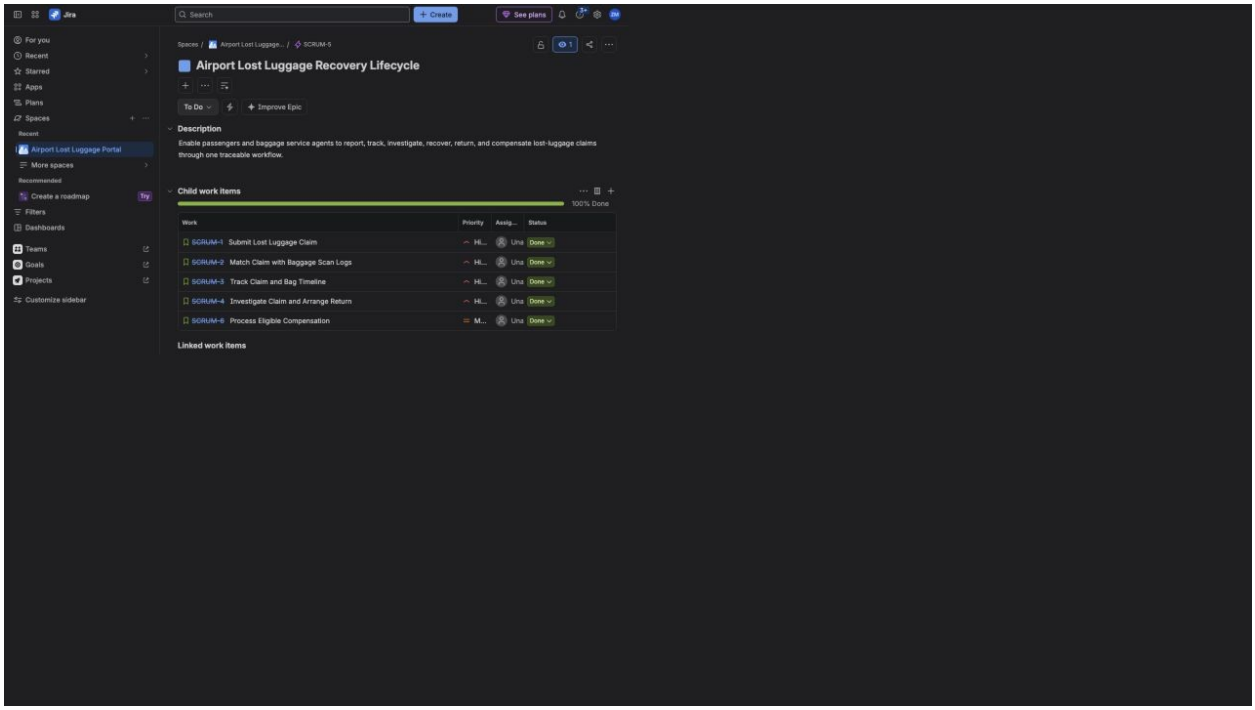


Figure 1. Jira epic and linked user stories.

4. Sprint Execution

Sprint Attribute	Configured Value
Sprint	SCRUM Sprint 1
Duration	One week: 2 September 2026 to 9 September 2026
Commitment	26 story points
Workflow simulation	To Do -> In Progress -> Done
Completion	5 of 5 stories completed; 26 of 26 points delivered

The active board initially placed all five committed stories in To Do. Each story was then moved through In Progress and completed in Done before the sprint was closed.

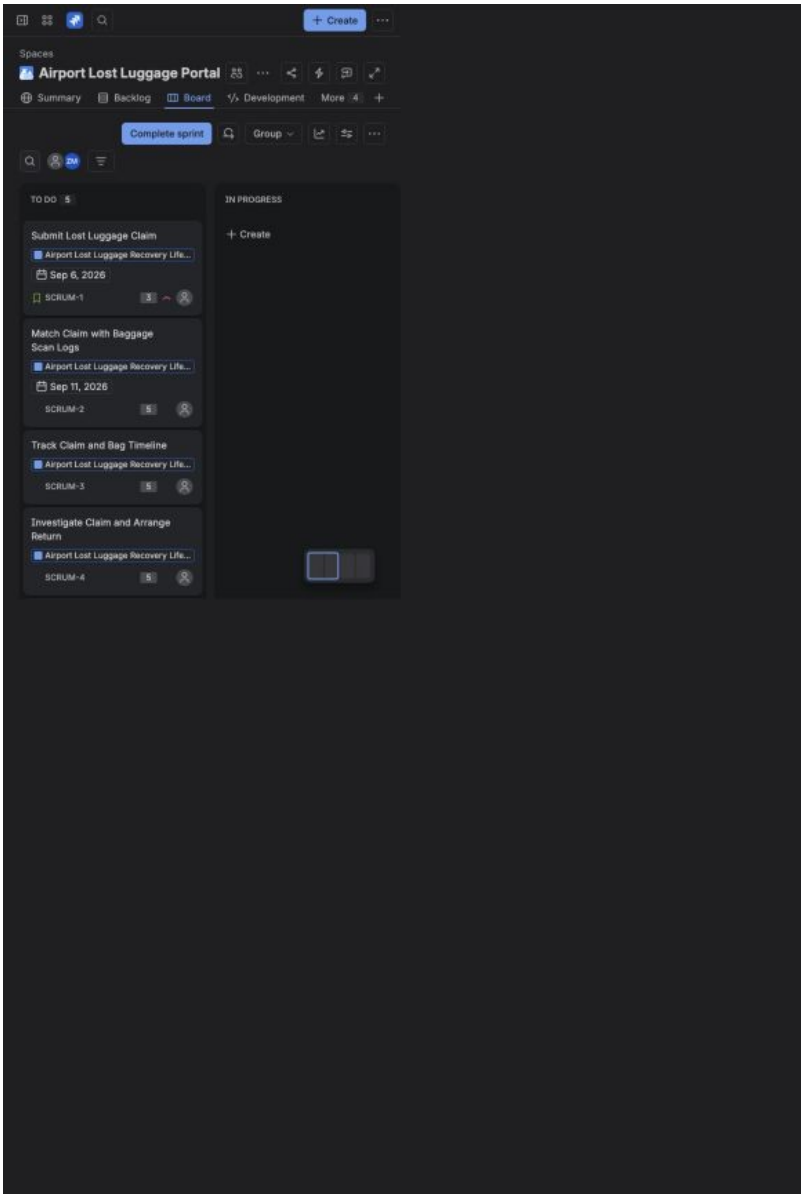


Figure 2. Active sprint board at the initial To Do state.

5. Burndown Evidence

The Jira burndown report records the full 26-point commitment reaching zero remaining points within the completed one-week sprint. The report is configured for SCRUM Sprint 1 and story-point estimation.

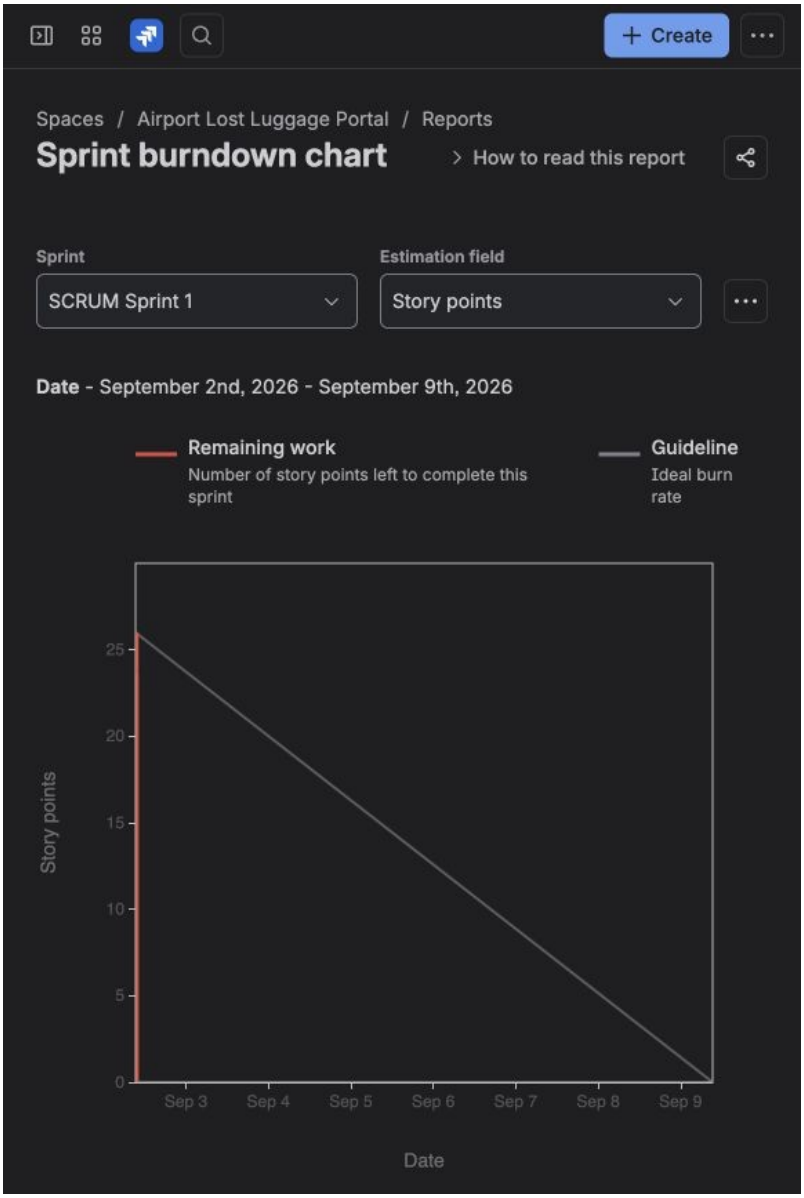


Figure 3. Jira burndown report for the completed sprint.

6. Reflection

1. Did the estimations reflect the actual effort?

Yes. The 3-point claim-submission story was the smallest bounded workflow, while scan matching, timeline tracking, and recovery coordination required more integration and validation. Compensation received the highest estimate because it combines eligibility rules, evidence checks, decision output, and payment-state handling.

2. Was the backlog well-prioritized?

Yes. High-priority work established the operational recovery path first: claim creation, scan matching, tracking, and agent-led return. Compensation followed at Medium priority because it depends on a mature, unresolved claim.

3. How did the simulated sprint align with expectations?

The sprint progressed logically from intake and scan matching to passenger visibility, agent recovery, and final compensation handling. The staged status changes made work-in-progress visible and preserved traceability before all five stories were completed.

4. What insights did the burndown provide?

The chart showed a single concentrated completion step because all status changes were simulated on the same day. In a real sprint, smaller stories should be closed continuously to provide steadier feedback and expose delivery risk earlier.
